structural

Hanover St Garage Restoration

Tue 8/30/22
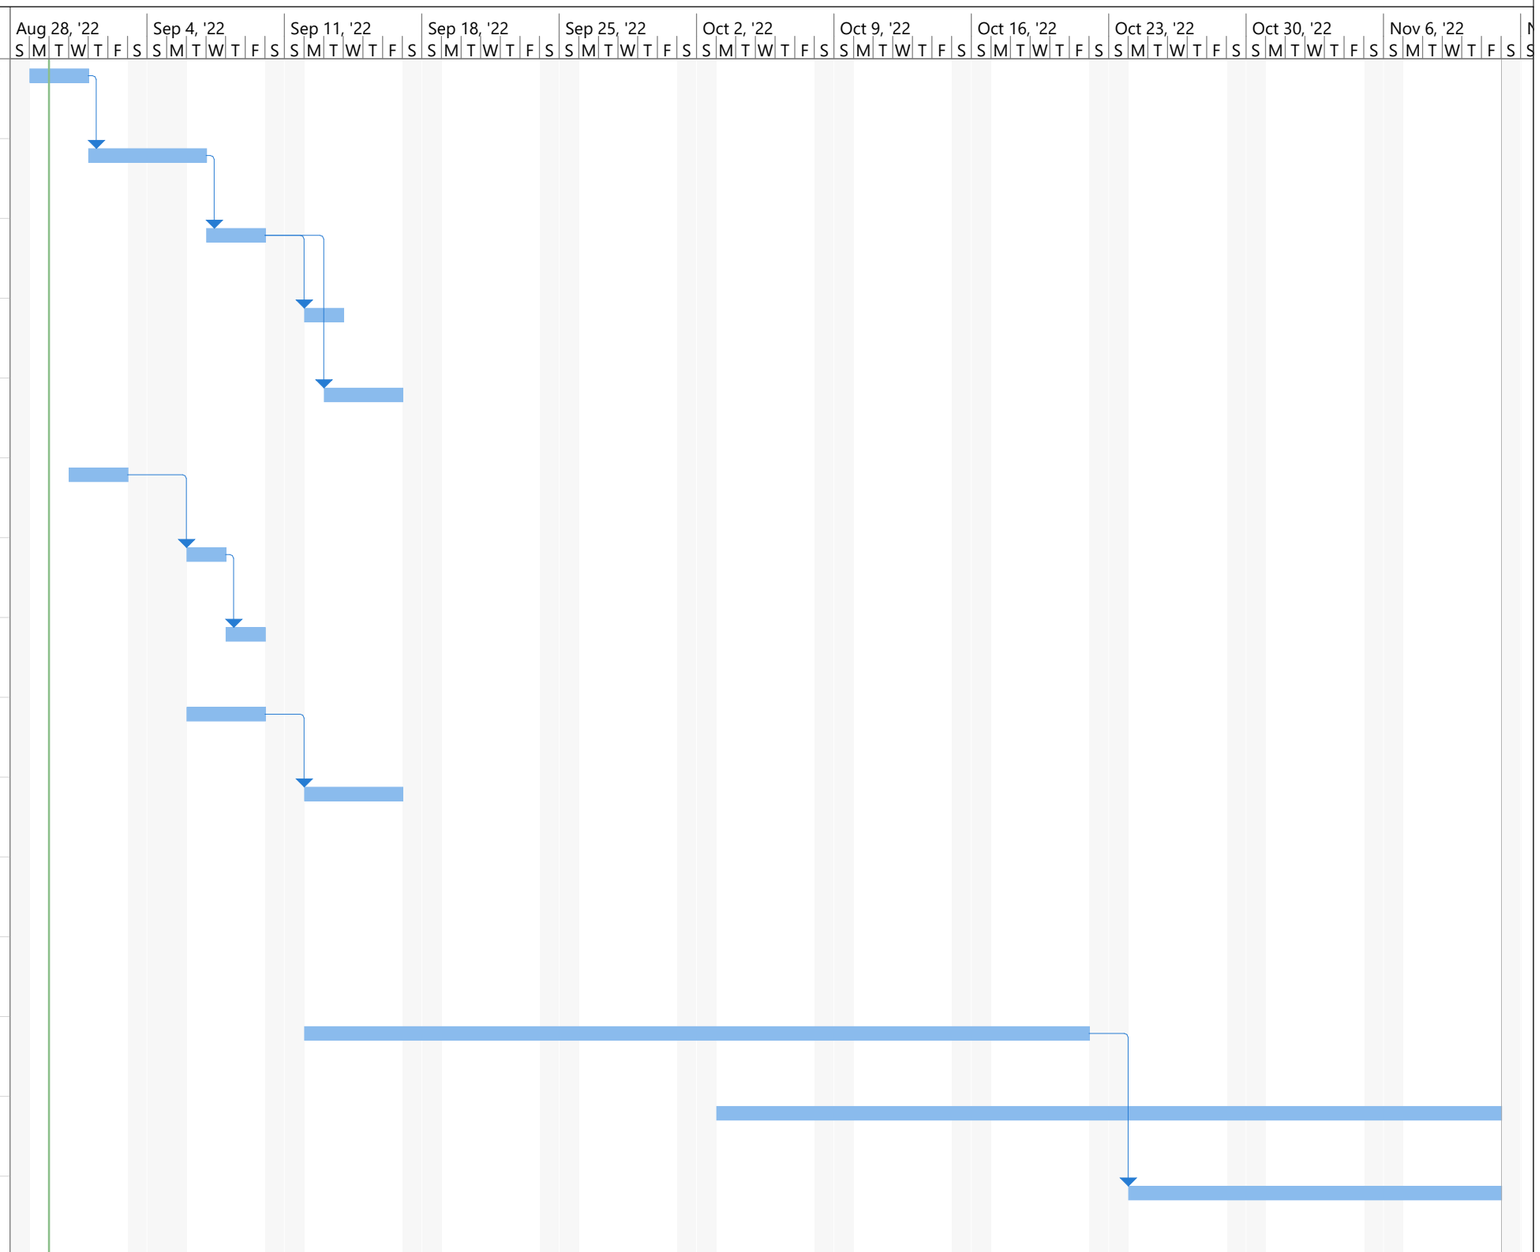
ID	Task Name	Duration	Start	Finish
1	Column Repair - Shoring (W.I. 6.6)	3 days	Mon 8/29/22	Wed 8/31/22
2	Column Repair - Demolition (W.I. 6.6)	3 days	Thu 9/1/22	Tue 9/6/22
3	Column Repair - Prep and Pour Back (W.I. 6	3 days	Wed 9/7/22	Fri 9/9/22
4	Column Repair - Clean, Install Mastic and Backfill (W.I. 6.6)	2 days	Mon 9/12/22	Tue 9/13/22
5	Column Repair - Shoring (W.I. 6.6)	4 days	Tue 9/13/22	Fri 9/16/22
6	Column Repair - Shoring (W.I. 6.7)	3 days	Wed 8/31/22	Fri 9/2/22
7	Column Repair - Demolition (W.I. 6.7)	2 days	Tue 9/6/22	Wed 9/7/22
8	Column Repair - Prep and Pour Back (W.I 6.	2 days	Thu 9/8/22	Fri 9/9/22
9	Concrete Repairs - Shoring Half of Phase 1	4 days	Tue 9/6/22	Fri 9/9/22
10	Concrete Repairs - Sawcut and Demolition (W.I. 3.1, 3.3, 3.6)	5 days	Mon 9/12/22	Fri 9/16/22
11				
12				
13	Masonry	30 days	Mon 9/12/22	Fri 10/21/22
14	Structural Steel	30 days	Mon 10/3/22	Fri 11/11/22
15	Standpipe Replacement	15 days	Mon 10/24/22	Fri 11/11/22
