Hanover St Garage Restoration

Wed 6/14/23
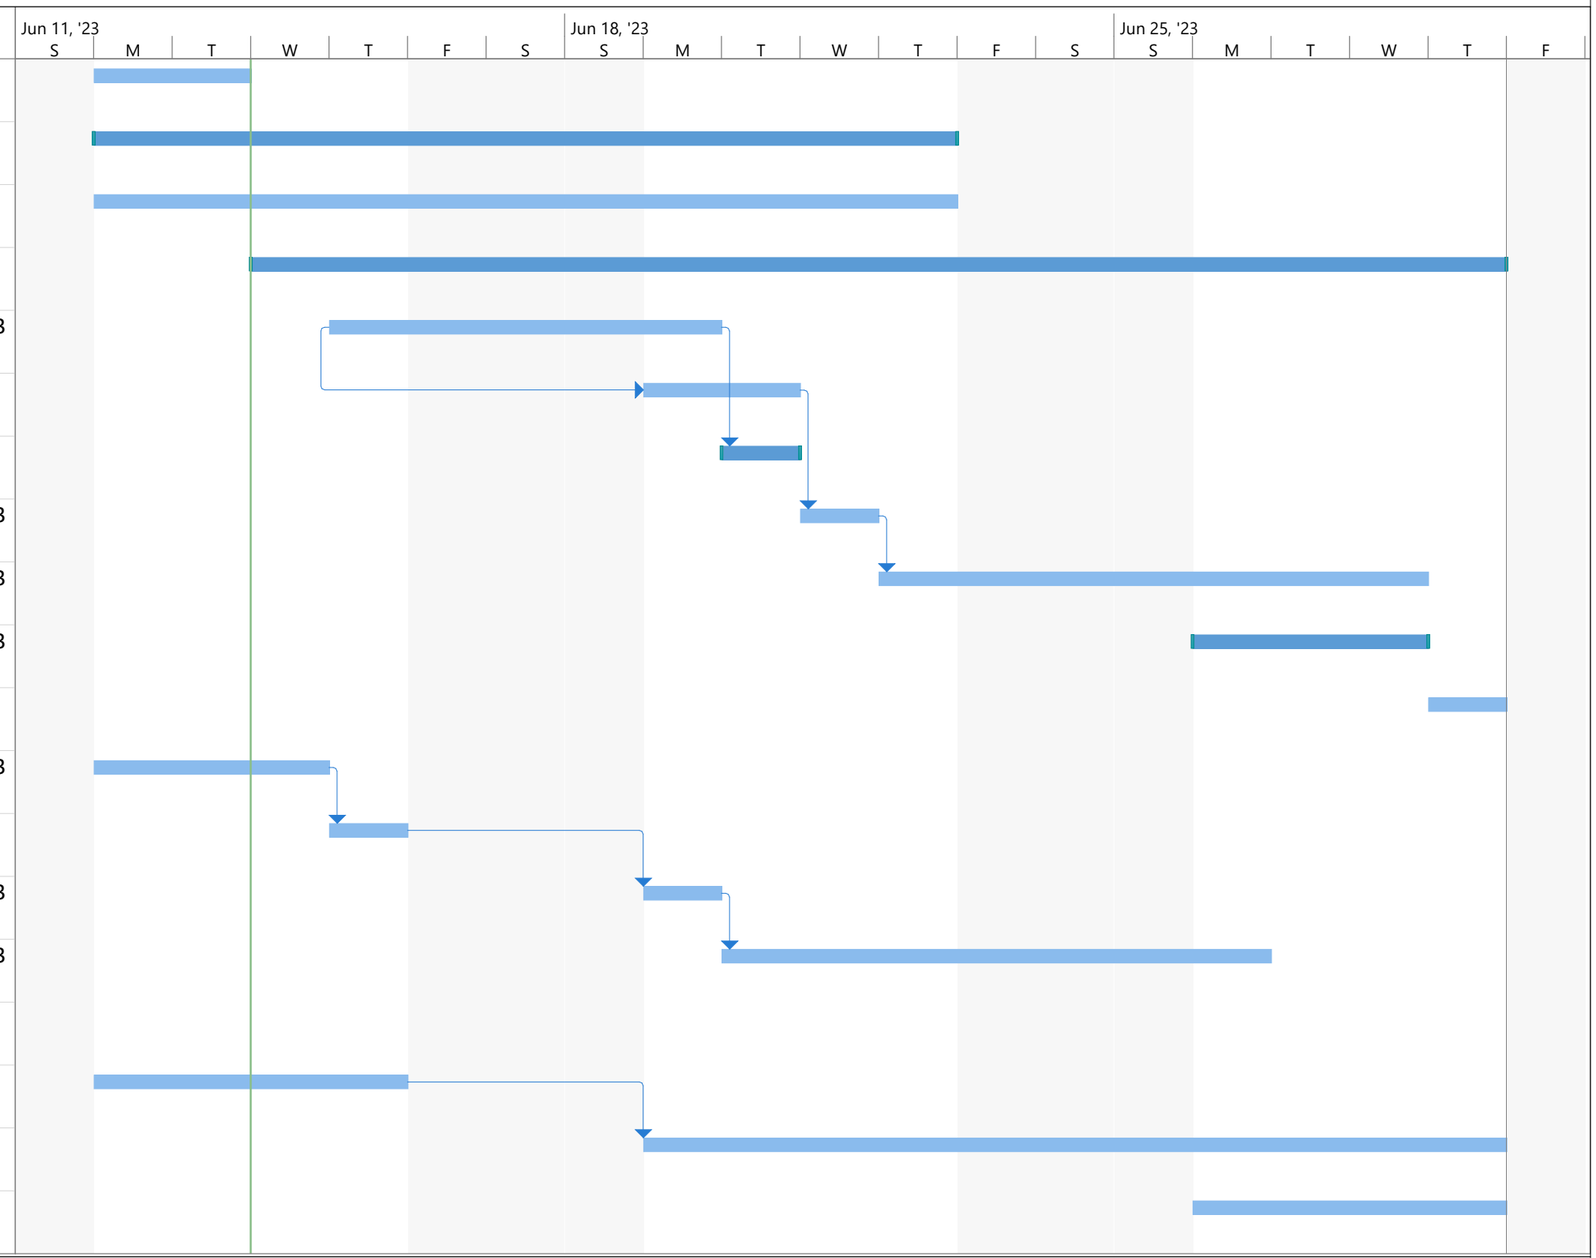
ID	Task Name	Duration	Start	Finish
1	Remove Temp Walls - Level 3	2 days	Mon 6/12/23	Tue 6/13/23
2	Drain Replacement (W.I. 25.2)	8 days	Mon 6/12/23	Thu 6/22/23
3	Caulking/Sealant Work - Level 3 (W.I. 11.1, 11.2, 11.4)	8 days	Mon 6/12/23	Thu 6/22/23
4	Expansion Joint - R/R Winged Joint (W.I. 10.3) - Levels 2 & 3	10 days	Wed 6/14/23	Thu 6/29/23
5	Concrete Repairs - Level 2 - Demolition (W.I. 3.1, 3.3)	2 days	Thu 6/15/23	Mon 6/19/23
6	Concrete Repairs - Level 2 - Rebar and Prep (W.I. 3.1, 3.3)	2 days	Mon 6/19/23	Tue 6/20/23
7	Concrete Repairs - Level 2 - Formwork (Only W.I. 3.3)	1 day	Tue 6/20/23	Tue 6/20/23
8	Concrete Repairs - Pour Back and Clean (W.I. 3.1, 3.3)	1 day	Wed 6/21/23	Wed 6/21/23
9	Curing Period for Level 2 floor repairs	4 days	Thu 6/22/23	Wed 6/28/23
10	Remove Temp Walls - Level 2	3 days	Mon 6/26/23	Wed 6/28/23
11	Remove Shoring for Level 2 floor repairs	1 day	Thu 6/29/23	Thu 6/29/23
12	Concrete Repairs - Level 2 - Demolition (W.I. 4.1, 4.2)	3 days	Mon 6/12/23	Wed 6/14/23
13	Concrete Repairs - Level 2 - Rebar and Prep (W.I. 4.1, 4.2)	1 day	Thu 6/15/23	Thu 6/15/23
14	Concrete Repairs - Pour Back and Clean (W.I. 4.1, 4.2)	1 day	Mon 6/19/23	Mon 6/19/23
15	Curing Period for OH Repairs	4 days	Tue 6/20/23	Mon 6/26/23
16				
17	Masonry Repairs - South Elevation	4 days	Mon 6/12/23	Thu 6/15/23
18	Masonry Repairs - North and West Elevations	8 days	Mon 6/19/23	Thu 6/29/23
19	Steel Repairs - 46.1D	4 days	Mon 6/26/23	Thu 6/29/23
