Hanover St Garage Restoration

Tue 7/25/23
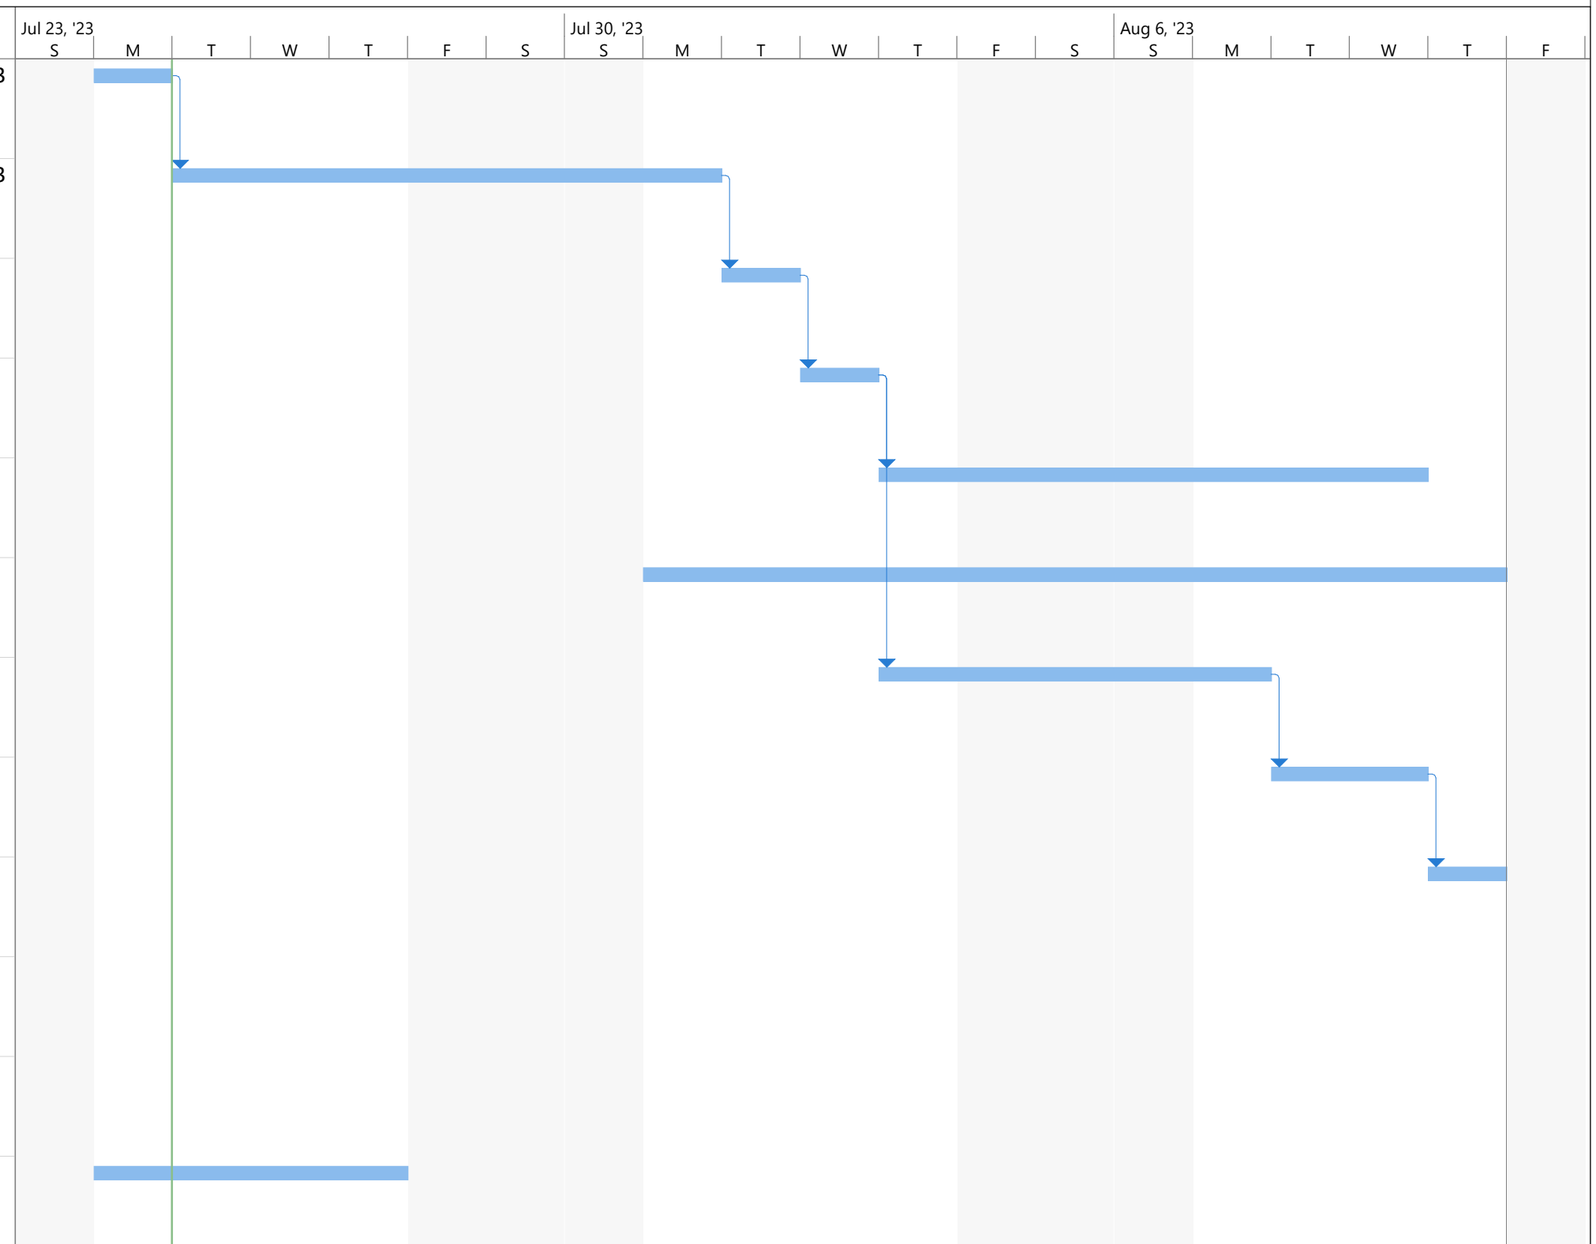
ID	Task Name	Duration	Start	Finish
1	Install Shoring - Level 3 Repairs	1 day	Mon 7/24/23	Mon 7/24/23
2	Concrete Repairs - Level 3 - Demolition Repairs (W.I. 3.1, 3.3)	4 days	Tue 7/25/23	Mon 7/31/23
3	Concrete Repairs - Level 3 - Rebar and Prep (W.I. 3.1, 3.6)	1 day	Tue 8/1/23	Tue 8/1/23
4	Concrete Repairs - Level 3 - Pour Back and Clean (W.I. 3.1, 3.3)	1 day	Wed 8/2/23	Wed 8/2/23
5	Curing period for level 3 concrete repairs	4 days	Thu 8/3/23	Wed 8/9/23
6	Caulking/Sealant Work - Level 3/4 (W.I. 11.1, 11.2, 11.4)	8 days	Mon 7/31/23	Thu 8/10/23
7	Install Temp Partitions - Level 2	2 days	Thu 8/3/23	Mon 8/7/23
8	Install Shoring - Level 3 Underside Repairs	2 days	Tue 8/8/23	Wed 8/9/23
9	Concrete Repairs - Underside of Level 3 - (W.I. 4.1, 4.2)	1 day	Thu 8/10/23	Thu 8/10/23
10				
11				
12	Steel Repairs - 46.1D	4 days	Mon 7/24/23	Thu 7/27/23
