Hanover St Garage Restoration

Tue 8/8/23
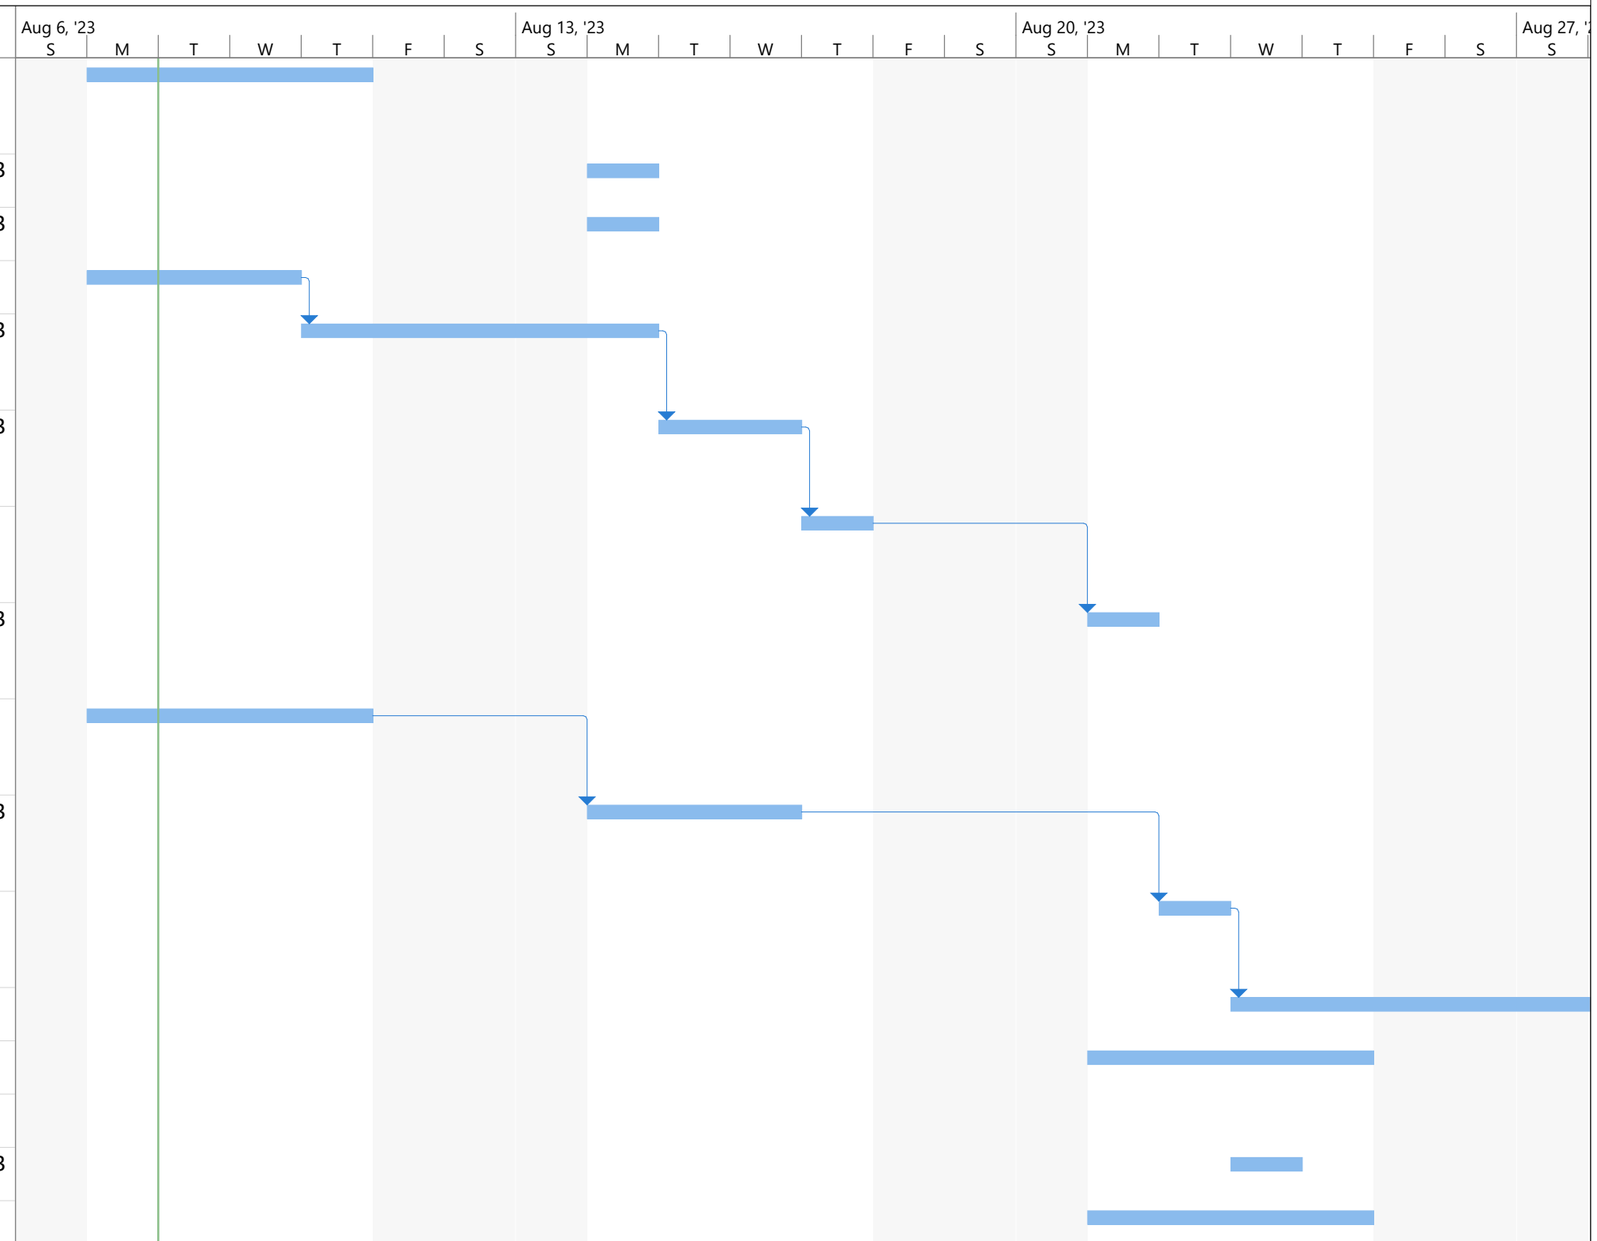
ID	Task Name	Duration	Start	Finish
1	Caulking/Sealant Work - Level 3/4 (W.I. 11.1, 11.2, 11.4)	4 days	Mon 8/7/23	Thu 8/10/23
2	Remove Temporary Walls - Level 3/4	1 day	Mon 8/14/23	Mon 8/14/23
3	Expansion Joint - Level 3/4 (W.I. 10.3, 10.5	1 day	Mon 8/14/23	Mon 8/14/23
4	Curing Period for Level 3/4 Concrete Repa	3 days	Mon 8/7/23	Wed 8/9/23
5	Remove Shoring - Level 3/4 Underside Repairs	2 days	Thu 8/10/23	Mon 8/14/23
6	Concrete Repairs - Underside of Level 3 - Demolition (W.I. 4.1, 4.2)	2 days	Tue 8/15/23	Wed 8/16/23
7	Concrete Repairs - Underside of Level 3 - Rebar and Prep (W.I. 4.1, 4.2)	1 day	Thu 8/17/23	Thu 8/17/23
8	Concrete Repairs - Underside of Level 3 - Pour Back and Clean (W.I. 4.1, 4.2)	1 day	Mon 8/21/23	Mon 8/21/23
9	Concrete Repairs - Level 2/3 - Demolition (W.I. 3.1, 3.3, 3.6)	4 days	Mon 8/7/23	Thu 8/10/23
10	Concrete Repairs - Level 2/3 Rebar and Prep (W.I. 3.1, 3.3, 3.6)	3 days	Mon 8/14/23	Wed 8/16/23
11	Concrete Repairs - Level 2/3 - Pour Back and Clean (W.I. 3.1, 3.3, 3.6)	1 day	Tue 8/22/23	Tue 8/22/23
12	Curing Period for Level 2/3 Concrete Repa	8 days	Wed 8/23/23	Tue 9/5/23
13	Install Drains (W.I. 25.2)	4 days	Mon 8/21/23	Thu 8/24/23
14				
15	Steel Repairs - 46.1D	1 day	Wed 8/23/23	Wed 8/23/23
16	APH	4 days	Mon 8/21/23	Thu 8/24/23
