structural

Hanover St. Garage Restoration - 2022

7/26/2022
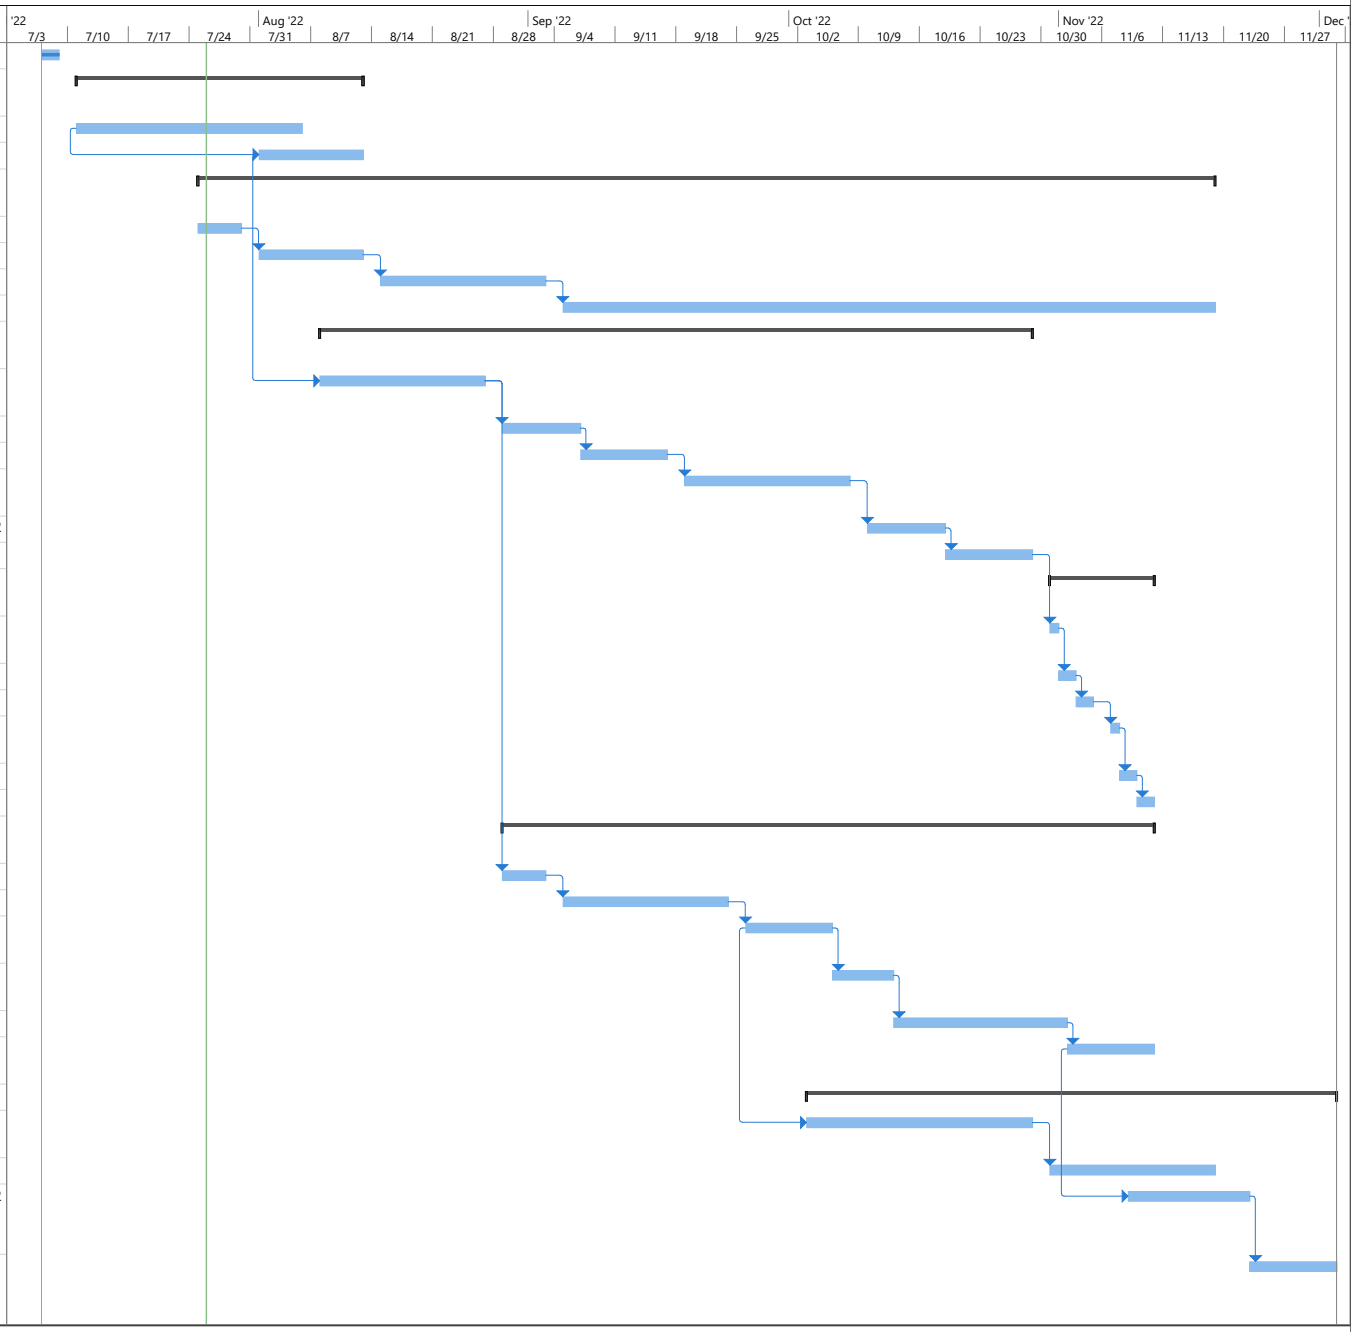
ID	Task Name	Duration	Start	Finish
1	**Mobilization**	**2 days**	**Thu 7/7/22**	**Fri 7/8/22**
2	**Site Safety and Construction Barrier Panels**	**25 days**	**Mon 7/11/22**	**Fri 8/12/22**
3	Build Panels	20 days	Mon 7/11/22	Fri 8/5/22
4	Move/Install Panels	10 days	Mon 8/1/22	Fri 8/12/22
5	**Strucutral Steel Repair - Level 2 & 3 underside**	**85 days**	**Mon 7/25/22**	**Fri 11/18/22**
6	Exploratory prep work	5 days	Mon 7/25/22	Fri 7/29/22
7	Shop Drawings	10 days	Mon 8/1/22	Fri 8/12/22
8	Field Measure and Fabrication	15 days	Mon 8/15/22	Fri 9/2/22
9	Installation	55 days	Mon 9/5/22	Fri 11/18/22
10	**Column Repair - Level 1 (W.I. 6.6)**	**60 days**	**Mon 8/8/22**	**Fri 10/28/22**
11	Shoring - Half of the total columns	15 days	Mon 8/8/22	Fri 8/26/22
12	Demolition	7 days	Mon 8/29/22	Tue 9/6/22
13	Prep and Pour Back	8 days	Wed 9/7/22	Fri 9/16/22
14	Shoring - Remaining half of the columns	15 days	Mon 9/19/22	Fri 10/7/22
15	Demolition	7 days	Mon 10/10/22	Tue 10/18/22
16	Prep and Pour Back	8 days	Wed 10/19/22	Fri 10/28/22
17	**Column Repair - Level 1 (W.I. 6.7)**	**10 days**	**Mon 10/31/22**	**Fri 11/11/22**
18	Shoring - Half of the total columns	1 day	Mon 10/31/22	Mon 10/31/22
19	Demolition	2 days	Tue 11/1/22	Wed 11/2/22
20	Prep and Pour Back	2 days	Thu 11/3/22	Fri 11/4/22
21	Shoring - Remaining half of the columns	1 day	Mon 11/7/22	Mon 11/7/22
22	Demolition	2 days	Tue 11/8/22	Wed 11/9/22
23	Prep and Pour Back	2 days	Thu 11/10/22	Fri 11/11/22
24	**Concrete Repairs - Level 3 - Phase 1**	**55 days**	**Mon 8/29/22**	**Fri 11/11/22**
25	Shoring - Half of phase 1	5 days	Mon 8/29/22	Fri 9/2/22
26	Demolition - W.I. 3.1, 3.3, 3.6	15 days	Mon 9/5/22	Fri 9/23/22
27	Prep and Pour Back - W.I. 3.1, 3.3, 3.6	8 days	Mon 9/26/22	Wed 10/5/22
28	Shoring - Remaining half of phase 1	5 days	Thu 10/6/22	Wed 10/12/22
29	Demolition - W.I. 3.1, 3.3, 3.6	14 days	Thu 10/13/22	Tue 11/1/22
30	Prep and Pour Back - W.I. 3.1, 3.3, 3.6	8 days	Wed 11/2/22	Fri 11/11/22
31	**Painting - Level 3 - Phase 1**	**45 days**	**Mon 10/3/22**	**Fri 12/2/22**
32	Prep and prime - Half of phase 1 area	20 days	Mon 10/3/22	Fri 10/28/22
33	Paint - Half of phase 1 area	15 days	Mon 10/31/22	Fri 11/18/22
34	Prep and prime - Remaining half of phase 1 (Weather dependent)	10 days	Wed 11/9/22	Tue 11/22/22
35	Paint - Remaining half of phase 1 (Weather dependent)	8 days	Wed 11/23/22	Fri 12/2/22
