Hanover St Garage Restoration

Tue 9/19/23
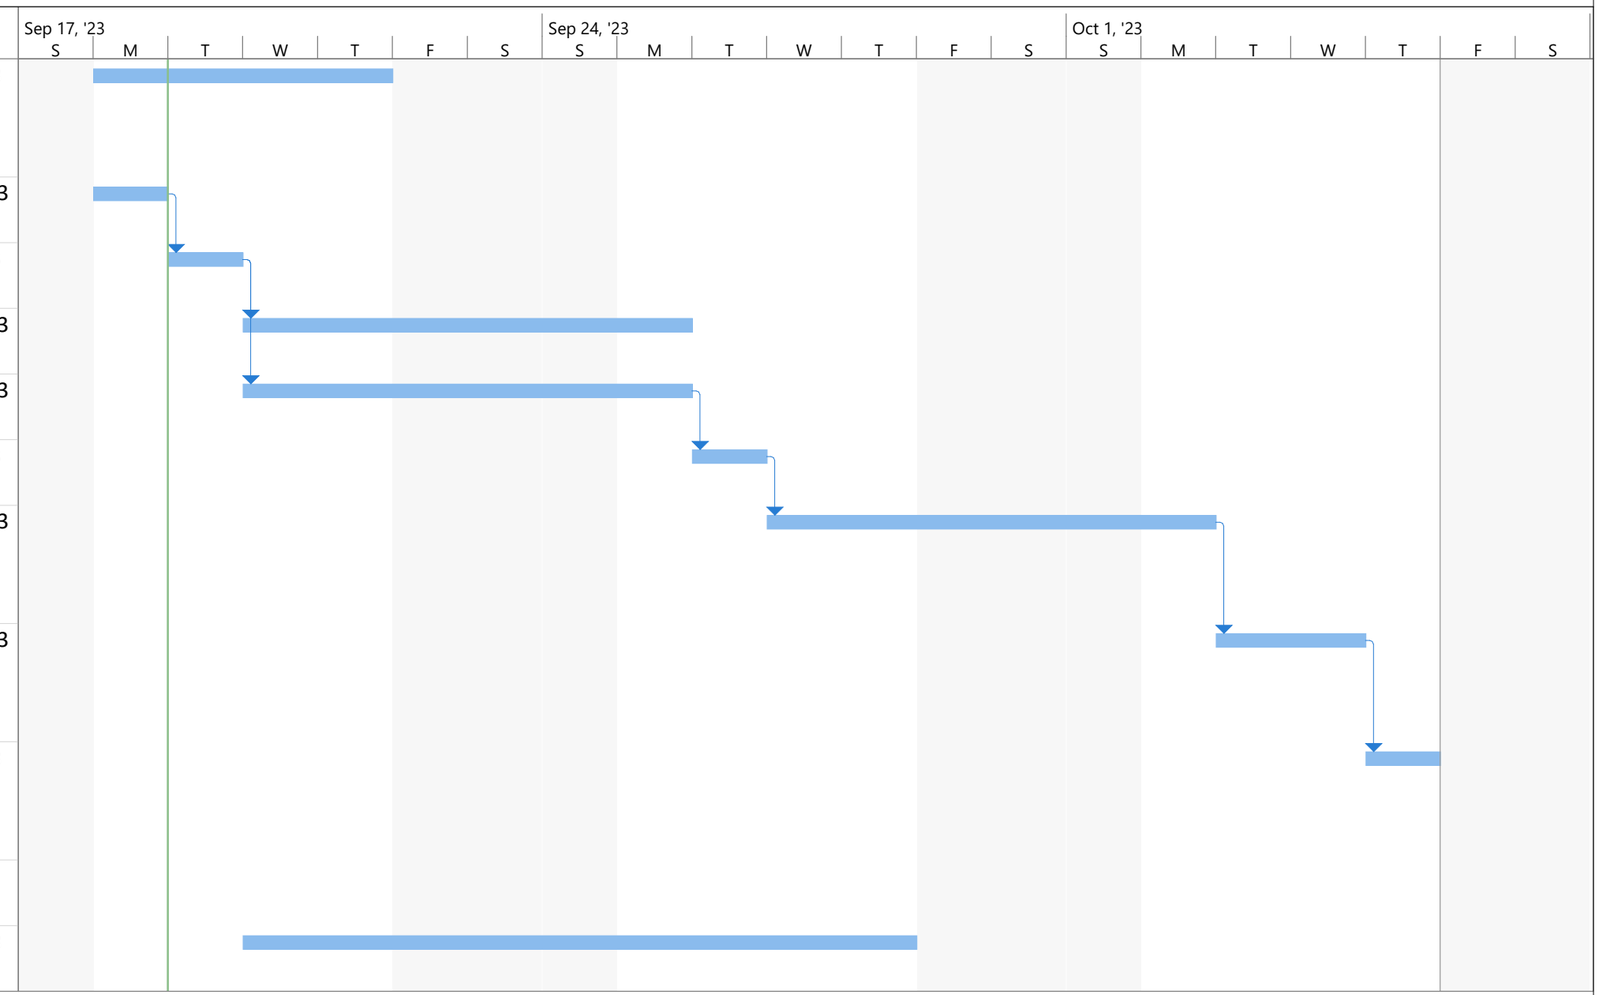
ID	Task Name	Duration	Start	Finish
1	Expansion Joint - Second Half of Level 2/3 and 3/4 Ramp (W.I. 10.3, 10.5)	4 days	Mon 9/18/23	Thu 9/21/23
2	Curing Period for Level 1/2 Concrete Repa	1 day	Mon 9/18/23	Mon 9/18/23
3	Remove Shoring Level 1	1 day	Tue 9/19/23	Tue 9/19/23
4	Change Phases/Move Temp Walls - Level 2	3 days	Wed 9/20/23	Mon 9/25/23
5	Change Phases/Move Temp Walls - Level 3	3 days	Wed 9/20/23	Mon 9/25/23
6	Install Shoring - Level 3 Repairs	1 day	Tue 9/26/23	Tue 9/26/23
7	Concrete Repairs - Level 3 - Demo (W.I. 3.1, 3.3, 3.6)	3 days	Wed 9/27/23	Mon 10/2/23
8	Concrete Repairs - Level 3 - Rebar/Prep (W.I. 3.1, 3.3, 3.6)	2 days	Tue 10/3/23	Wed 10/4/23
9	Concrete Repairs - Level 3 - Pour (W.I. 3.1, 3.3, 3.6)	1 day	Thu 10/5/23	Thu 10/5/23
10				
11	Plumbing Work	6 days	Wed 9/20/23	Thu 9/28/23
