Hanover St Garage Restoration

Tue 1/17/23
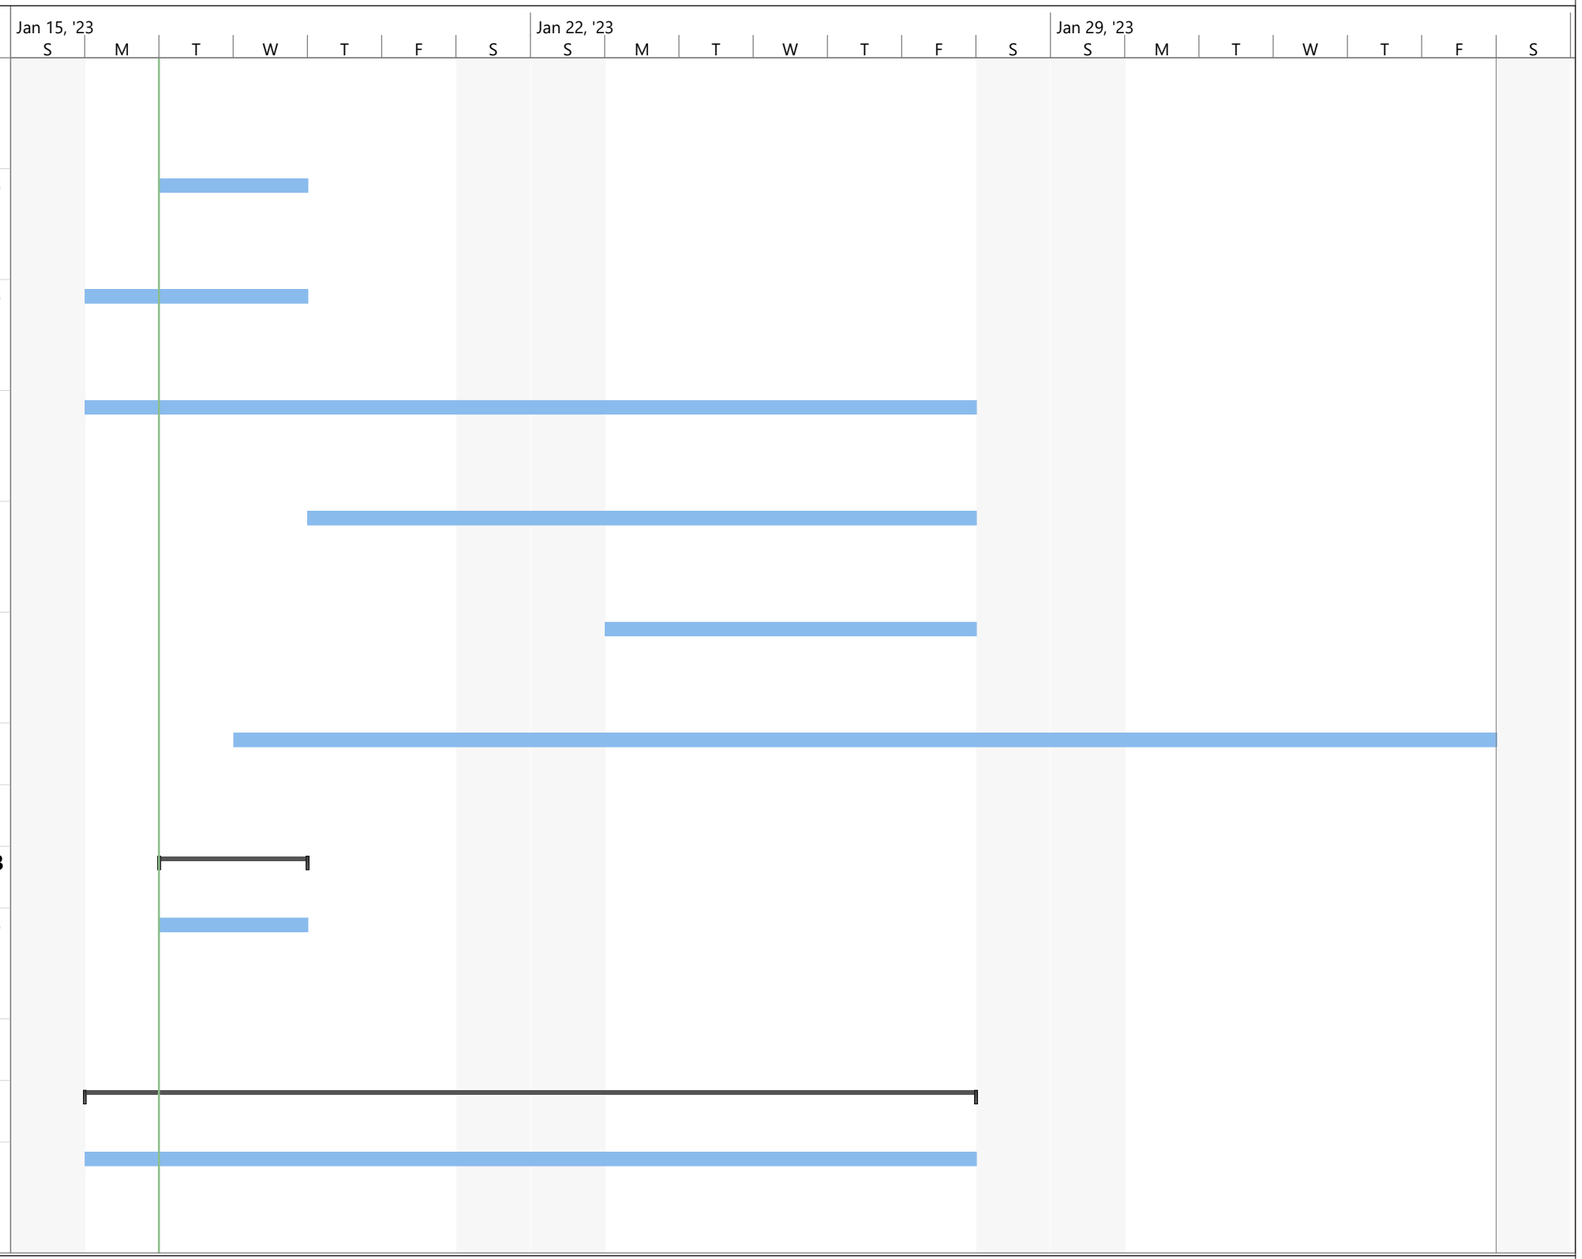
ID	Task Name	Duration	Start	Finish
1	Concrete Repairs - Prep and Rebar (W.I. 4.1, 4.2)	2 days	Thu 1/12/23	Fri 1/13/23
2	Concrete Repairs - Pour back and Clean (W.I. 4.1, 4.2)	2 days	Tue 1/17/23	Wed 1/18/23
3	Concrete Repairs - Shoring Installation (W.I. 3.1, 3.3, 3.6)	3 days	Mon 1/16/23	Wed 1/18/23
4	Concrete Repairs - Sawcut and Demolition (W.I. 3.1, 3.3, 3.6)	10 days	Mon 1/16/23	Fri 1/27/23
5	Concrete Repairs - Rebar and Prep (W.I. 3.1, 3.3, 3.6)	7 days	Thu 1/19/23	Fri 1/27/23
6	Concrete Repairs - Demolition (W.I. 4.1, 4.2)	5 days	Mon 1/23/23	Fri 1/27/23
7	Control Joint/Sealant Work	13 days	Wed 1/18/23	Fri 2/3/23
8				
9	**Structural Steel**	**2 days**	**Tue 1/17/23**	**Wed 1/18/23**
10	Structural Steel Repairs (W.I. 46.1B & 46.1C)	2 days	Tue 1/17/23	Wed 1/18/23
11				
12	**Standpipe**	**10 days**	**Mon 1/16/23**	**Fri 1/27/23**
13	Fire Standpipe Replacement - Installation (W.I 26.2)	10 days	Mon 1/16/23	Fri 1/27/23
