Hanover St Garage Restoration

Tue 2/21/23
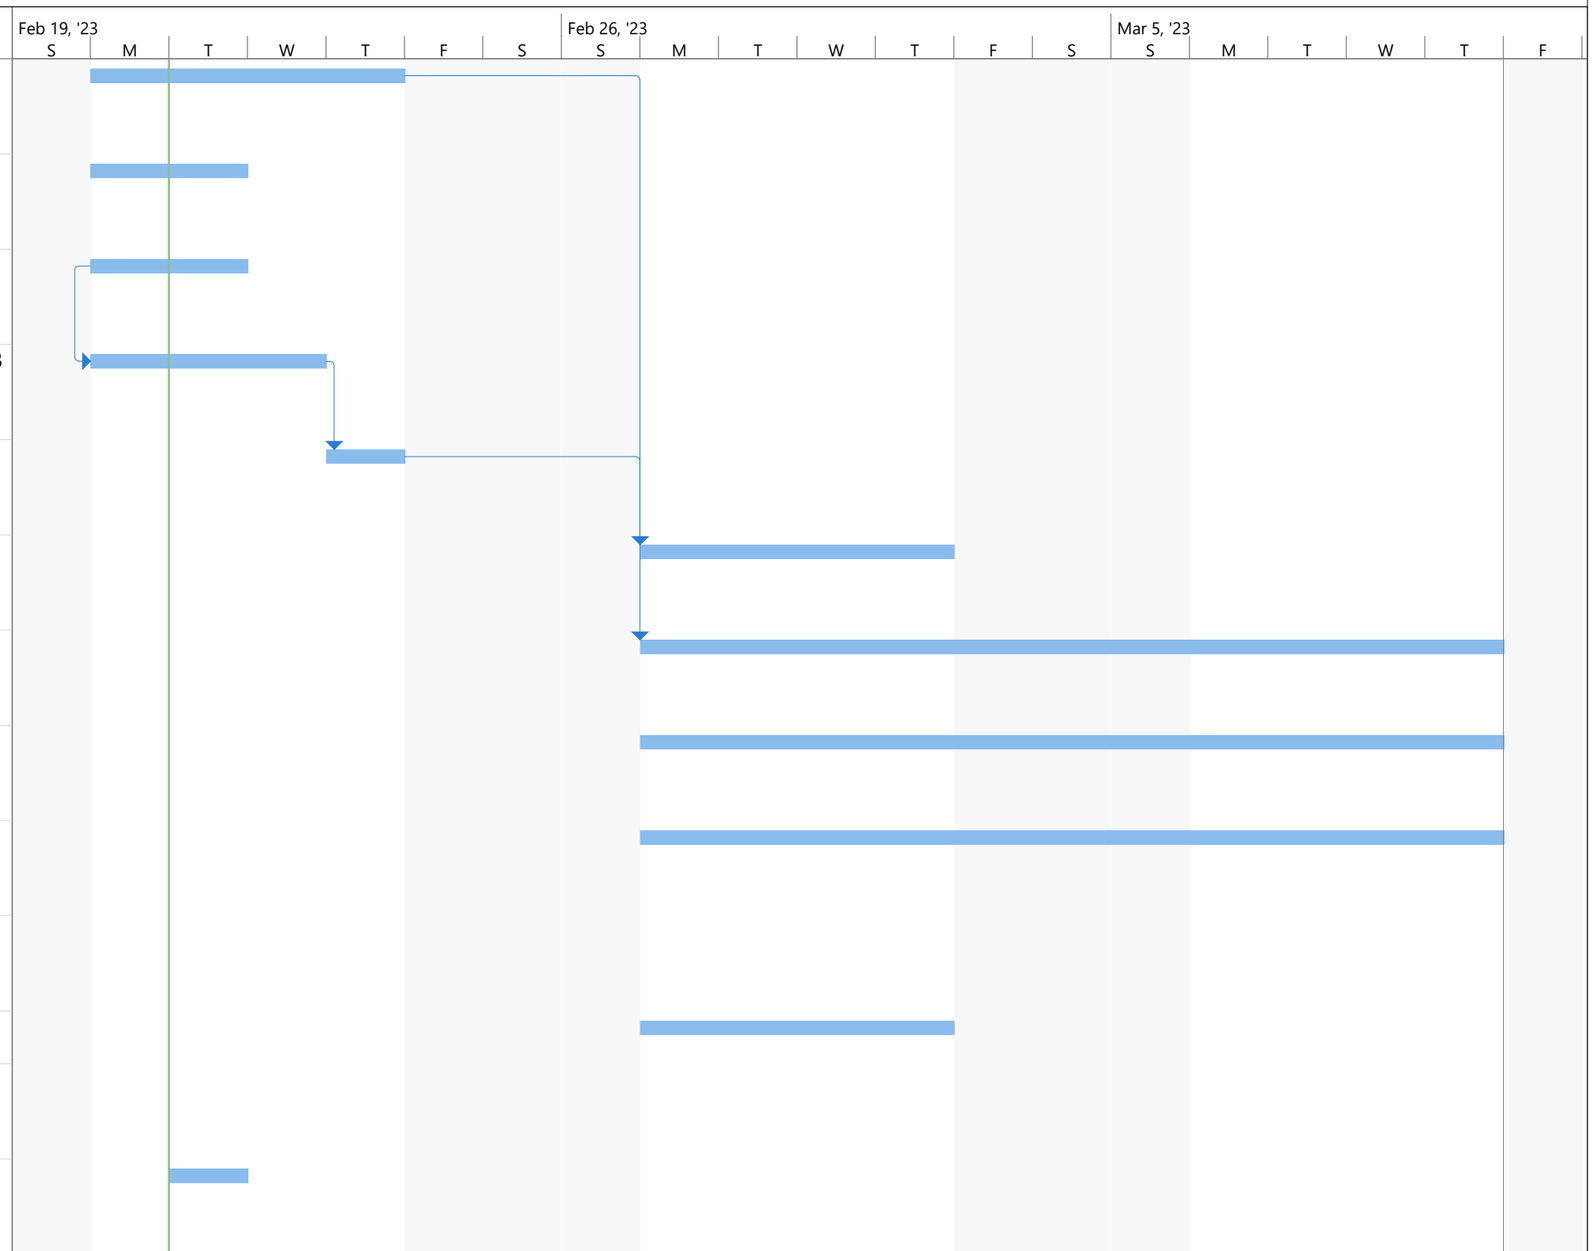
ID	Task Name	Duration	Start	Finish
1	Curing Period	4 days	Mon 2/20/23	Thu 2/23/23
2	Caulking/Sealant Work - Level 3	2 days	Mon 2/20/23	Tue 2/21/23
3	Concrete Repairs - Level 2 - Demolition (W.I. 3.1, 3.3, 3.6)	2 days	Mon 2/20/23	Tue 2/21/23
4	Concrete Repairs - Level 2 - Rebar and Prep (W.I. 3.1, 3.3, 3.6)	3 days	Mon 2/20/23	Wed 2/22/23
5	Concrete Repairs - Pour Back and Clean (W.I. 3.1, 3.3, 3.6)	1 day	Thu 2/23/23	Thu 2/23/23
6	Curing Period	4 days	Mon 2/27/23	Thu 3/2/23
7	Caulking/Sealant Work - Level 2	8 days	Mon 2/27/23	Thu 3/9/23
8	Concrete Repairs - Pour Back with Prepackaged Mortar and Clean (W.I. 3.1)	8 days	Mon 2/27/23	Thu 3/9/23
9	Expansion Joint Replacement	8 days	Mon 2/27/23	Thu 3/9/23
10				
11	Steel Repairs - 46.1C	4 days	Mon 2/27/23	Thu 3/2/23
12				
13	Electric Relocation	1 day	Tue 2/21/23	Tue 2/21/23
